


埼玉高速鉄道沿線土地区画整理事業進捗状況

平成25年3月末現在

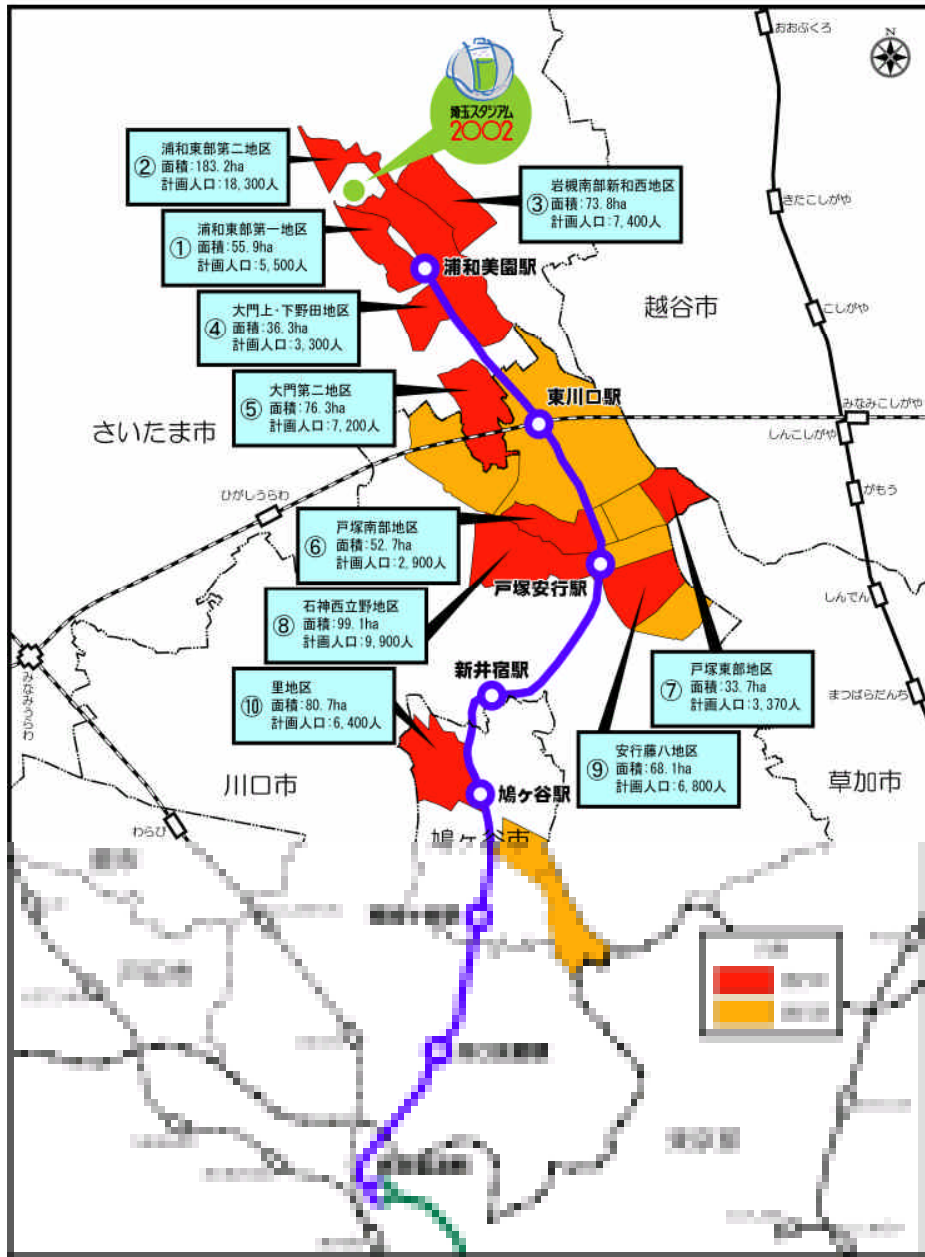

番号	市町村名	地区名	施行主体	面積 (ha)	施行期間	計画人口 (人)	総事業費 (百万円) うち国庫補助等	進捗率(%)														
								事業費ベース					仮換地指定率					使用収益開始率				
								20年度末	21年度末	22年度末	23年度末	24年度末	20年度末	21年度末	22年度末	23年度末	24年度末	20年度末	21年度末	22年度末	23年度末	24年度末
①	さいたま市	浦和東部第一	市	55.9	H12~H31	5,500	21,840 7,485	26.6%	35.1%	46.3%	52.5%	59.0%	100.0%	100.0%	100.0%	100.0%	100.0%	0.0%	0.0%	0.0%	0.0%	0.0%
②	さいたま市	浦和東部第二	機構	183.2	H12~H30	18,300	67,496 20,543	57.8%	70.1%	82.5%	88.3%	94.3%	54.0%	58.2%	63.9%	81.6%	93.7%	29.8%	33.7%	34.1%	34.8%	47.1%
③	さいたま市	岩槻南部新和西	機構	73.8	H12~H30	7,400	30,771 8,240	40.4%	49.5%	64.5%	78.6%	90.5%	6.7%	13.0%	34.3%	40.5%	73.9%	3.8%	4.3%	7.7%	8.4%	8.4%
④	さいたま市	大門上・下野田	組合	36.3	H6~H26	3,300	10,742 4,424	57.2%	63.2%	68.1%	72.8%	76.0%	96.2%	96.2%	96.2%	100.0%	100.0%	0.0%	0.0%	0.0%	10.9%	41.3%
⑤	さいたま市	大門第二	組合	76.3	H4~H27	7,200	26,910 8,450	29.0%	31.4%	33.6%	36.8%	39.5%	100.0%	100.0%	100.0%	100.0%	100.0%	0.0%	0.0%	0.0%	0.0%	0.0%
⑥	川口市	戸塚南部	組合	52.7	S62~H30	2,900	15,950 9,318	92.5%	93.7%	96.1%	96.9%	98.3%	100.0%	100.0%	100.0%	100.0%	100.0%	82.9%	88.4%	90.5%	90.7%	91.0%
⑦	川口市	戸塚東部	組合	33.7	H5~H31	3,370	15,646 7,589	53.7%	58.4%	61.8%	64.3%	64.4%	100.0%	100.0%	100.0%	100.0%	100.0%	24.4%	25.4%	29.1%	29.3%	30.8%
⑧	川口市	石神西立野	市	99.1	H6~H35	9,900	36,100 20,384	22.2%	25.4%	28.3%	30.4%	32.6%	93.2%	93.9%	94.0%	94.7%	94.6%	10.5%	12.2%	13.1%	14.2%	14.9%
⑨	川口市	安行藤八	市	68.1	H9~H36	6,800	30,675 20,403	8.6%	10.4%	12.1%	13.4%	15.1%	90.7%	91.5%	91.7%	93.1%	93.2%	18.1%	19.3%	20.1%	20.7%	22.0%
⑩	鳩ヶ谷市	里	市	80.7	H1~H35	6,400	37,590 23,992	58.1%	62.3%	66.2%	69.1%	71.3%	100.0%	100.0%	100.0%	100.0%	100.0%	28.8%	37.6%	41.4%	45.4%	46.6%
合計				759.8		71,070	293,720 130,828	43.2%	49.5%	56.5%	61.1%	65.4%	80.5%	82.1%	85.1%	89.7%	95.1%	20.5%	23.2%	24.5%	26.0%	30.6%

※1 データは、平成24年度「彩の国の区画整理」(H25.6作成)から。  
 ※2 国庫補助等は、基本事業費、一般会計補助事業費、地方特定道路整備事業の合計。  
 ※3 定着人口(H24年度末) さいたま市(6,734人) 川口市(22,079人)

埼玉高速鉄道沿線土地区画整理事業進捗状況(施行中)

平成25年3月末現在

黄色着色部に入力をお願いします

号	市町村名	地区名	施行主体	13年度末	14年度末	15年度末	16年度末	17年度末	18年度末	19年度末	20年度末	21年度末	22年度末	23年度末	24年度末			
①	さいたま市	浦和東部第一	市	面積(ha)	55.9	55.9	55.9	55.9	55.9	55.9	55.9	55.9	55.9	55.9	55.9			
				施行期間	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	H12-H31	
				計画人口(人)	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	5,500	
				総事業費	18,884	18,884	18,884	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840
					うち国庫補助等	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485	7,485
				事業費ベース	総事業費	18,884	18,884	18,884	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840	21,840
					執行済額	0	227	642	917	1,594	2,577	3,866	5,809	7,666	10,112	11,466	12,886	
				進捗率			1.2%	3.4%	4.2%	7.3%	11.8%	17.7%	26.6%	35.1%	46.3%	52.5%	59.0%	
					仮換地指定率	仮換地総面積	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	
					仮換地指定率				100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	
				使用収益	仮換地総面積	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	31.9	
					使用収益済面積	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
				使用収益開始率				0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	
②	さいたま市	浦和東部第二	機構	面積(ha)	183.2	183.2	183.2	183.2	183.2	183.2	183.2	183.2	183.2	183.2	183.2			
				施行期間	H12-H31	H12-H31	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30	H12-H30		
				計画人口(人)	18,300	18,300	18,300	18,300	18,300	18,300	18,300	18,300	18,300	18,300	18,300	18,300		
				総事業費	67,496	67,496	76,266	72,464	72,464	67,496	67,496	67,496	67,496	67,496	67,496	67,496		
					うち国庫補助等	20,543	20,543	20,543	20,543	21,543	20,543	20,543	20,543	20,543	20,543	20,543	20,543	
				事業費ベース	総事業費	67,496	67,496	76,266	72,464	72,464	67,496	67,496	67,496	67,496	67,496	67,496		
					執行済額	0	10,124	10,982	14,783	21,884	21,396	24,434	39,013	47,315	55,684	59,599	63,649	
				進捗率			15.0%	14.4%	20.4%	30.2%	31.7%	36.2%	57.8%	70.1%	82.5%	88.3%	94.3%	
					仮換地指定率	仮換地総面積	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	20.4	39.3	49.5	52.9	50.7	54.6	59.9	76.5	87.9	
					仮換地指定率				21.7%	41.9%	52.8%	56.4%	54.0%	58.2%	63.9%	81.6%	93.7%	
				使用収益	仮換地総面積	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8	93.8		
					使用収益済面積	0.0	0.0	0.0	0.0	14.5	23.2	24.1	28.0	31.6	32.0	32.6	44.2	
				使用収益開始率				0.0%	15.5%	24.7%	25.7%	29.8%	33.7%	34.1%	34.8%	47.1%		
③	さいたま市	岩槻南部新和西	機構	面積(ha)	73.8	73.8	73.8	73.8	73.8	73.8	73.8	73.8	73.8	73.8	73.8			
				施行期間	H12-H27	H12-H27	H12-H27	H12-H27	H12-H27	H12-H27	H12-H27	H12-H27	H12-H30	H12-H30	H12-H30	H12-H30		
				計画人口(人)	7,400	7,400	7,400	7,400	7,400	7,400	7,400	7,400	7,400	7,400	7,400	7,400		
				総事業費	28,364	28,364	30,799	28,364	28,364	28,364	28,364	28,364	28,364	30,771	30,771	30,771		
					うち国庫補助等	6,086	6,086	6,086	6,086	6,086	6,086	6,086	6,086	8,240	8,240	8,240		
				事業費ベース	総事業費	28,364	28,364	30,799	28,364	28,364	28,364	28,364	28,364	30,771	30,771	30,771		
					執行済額	0	4,822	3,542	4,425	7,460	7,318	9,076	11,459	15,232	19,847	24,186	27,848	
				進捗率			17.0%	11.5%	15.6%	26.3%	25.8%	32.0%	40.4%	49.5%	64.5%	78.6%	90.5%	
					仮換地指定率	仮換地総面積	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	0.0	0.1	0.3	0.9	2.6	5.0	13.1	15.5	28.3	
					仮換地指定率				0.0%	0.3%	0.9%	2.4%	6.7%	13.0%	34.3%	40.5%	73.9%	
				使用収益	仮換地総面積	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3	38.3		
					使用収益済面積	0.0	0.0	0.0	0.0	0.0	0.0	0.4	1.5	1.6	2.9	3.2	3.2	
				使用収益開始率				0.0%	0.0%	0.0%	1.1%	3.8%	4.3%	7.7%	8.4%	8.4%		
④	さいたま市	大門上・下野田	組合	面積(ha)	36.3	36.3	36.3	36.3	36.3	36.3	36.3	36.3	36.3	36.3	36.3			
				施行期間	H6-H15	H6-H15	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26	H6-H26		
				計画人口(人)	3,300	3,300	3,300	3,300	3,300	3,300	3,300	3,300	3,300	3,300	3,300	3,300		
				総事業費	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742		
					うち国庫補助等	4,424	4,424	4,424	4,424	4,424	4,424	4,424	4,424	4,424	4,424	4,424		
				事業費ベース	総事業費	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742	10,742		
					執行済額	0	2,019	2,234	2,857	3,609	4,436	5,360	6,144	6,789	7,315	7,820	8,164	
				進捗率			18.8%	20.8%	26.6%	33.6%	41.3%	49.9%	57.2%	63.2%	68.1%	72.8%	76.0%	
					仮換地指定率	仮換地総面積	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	22.5	23.2	23.2	23.2	23.2	23.2	23.2	24.1	24.1	
					仮換地指定率				93.2%	96.2%	96.2%	96.2%	96.2%	96.2%	96.2%	100.0%	100.0%	
				使用収益	仮換地総面積	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1	24.1		
					使用収益済面積	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	2.6	10.0	
				使用収益開始率				0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	10.9%	41.3%		

埼玉高速鉄道沿線土地区画整理事業進捗状況(施行中)

平成25年3月末現在

黄色着色部に入力をお願いします

号	市町村名	地区名	施行主体	13年度末	14年度末	15年度末	16年度末	17年度末	18年度末	19年度末	20年度末	21年度末	22年度末	23年度末	24年度末				
⑤	さいたま市	大門第二	組合	面積(ha)	76.3	76.3	76.3	76.3	76.3	76.3	76.3	76.3	76.3	76.3	76.3				
				施行期間	H4-H17	H4-H17	H4-H17	H4-H17	H4-H17	H4-H27	H4-H27	H4-H27	H4-H27	H4-H27	H4-H27	H4-H27	H4-H27		
				計画人口(人)	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	7,200	
				総事業費	26,910	26,910	26,530	26,531	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910
					うち国庫補助等	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450	8,450
				事業費ベース	総事業費	26,910	26,910	26,530	26,531	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910	26,910
					執行済額	0	3,956	4,643	4,776	5,651	6,405	6,997	7,804	8,450	9,042	9,903	10,629		
				進捗率			14.7%	17.5%	18.0%	21.0%	23.8%	26.0%	29.0%	31.4%	33.6%	36.8%	39.5%		
					仮換地指定率	仮換地総面積	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	50.9	50.9	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	
					仮換地指定率				99.8%	99.8%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	
				使用収益	仮換地総面積	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	51.0	
					使用収益済面積	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
				使用収益開始率					0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%		
⑥	川口市	戸塚南部	組合	面積(ha)	52.7	52.7	52.7	52.7	52.7	52.7	52.7	52.7	52.7	52.7	52.7				
				施行期間	S62-H15	S62-H15	S62-H19	S62-H19	S62-H19	S62-H24	S62-H24	S62-H24	S62-H27	S62-H27	S62-H27	S62-H30			
				計画人口(人)	2,900	2,900	2,900	2,900	2,900	2,900	2,900	2,900	2,900	2,900	2,900	2,900			
				総事業費	15,515	15,515	15,515	15,515	15,628	15,628	15,628	15,628	15,628	15,950	15,950	15,950	15,950		
					うち国庫補助等	7,885	7,885	7,885	7,885	7,885	7,885	7,885	7,885	8,746	8,746	8,746	9,318		
				事業費ベース	総事業費	15,515	15,515	15,515	15,515	15,628	15,628	15,628	15,628	15,950	15,950	15,950	15,950		
					執行済額	0	10,240	8,983	10,892	11,408	13,174	13,815	14,456	14,945	15,328	15,456	15,679		
				進捗率			66.0%	57.9%	70.2%	73.0%	84.3%	88.4%	92.5%	93.7%	96.1%	96.9%	98.3%		
					仮換地指定率	仮換地総面積	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2		
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	35.1	35.1	35.2	35.2	35.2	35.2	35.2	35.2	35.2		
					仮換地指定率				99.8%	99.8%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%		
				使用収益	仮換地総面積	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2	35.2		
					使用収益済面積	0.0	0.0	0.0	23.9	25.2	28.1	29.2	29.2	31.1	31.9	31.9	32.0		
				使用収益開始率				67.8%	71.5%	79.7%	82.9%	88.4%	90.5%	90.7%	91.0%				
⑦	川口市	戸塚東部	組合	面積(ha)	33.7	33.7	33.7	33.7	33.7	33.7	33.7	33.7	33.7	33.7	33.7				
				施行期間	H5-H19	H5-H19	H5-H19	H5-H19	H5-H19	H5-H26	H5-H26	H5-H26	H5-H26	H5-H26	H5-H26	H5-H31			
				計画人口(人)	3,370	3,370	3,370	3,370	3,370	3,370	3,370	3,370	3,370	3,370	3,370	3,370			
				総事業費	15,200	15,200	15,200	15,200	14,836	14,836	14,836	14,836	14,836	14,836	14,836	14,836	15,646		
					うち国庫補助等	6,598	6,598	6,598	6,598	6,598	6,598	6,598	6,598	6,598	6,598	6,598	7,589		
				事業費ベース	総事業費	15,200	15,200	15,200	15,200	14,836	14,836	14,836	14,836	14,836	14,836	14,836	15,646		
					執行済額	0	5,487	4,043	4,849	5,207	6,454	6,988	7,967	8,664	9,169	9,540	10,076		
				進捗率			36.1%	26.6%	31.9%	35.1%	43.5%	47.1%	53.7%	58.4%	61.8%	64.3%	64.4%		
					仮換地指定率	仮換地総面積	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8		
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8		
					仮換地指定率				100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%		
				使用収益	仮換地総面積	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8	18.8		
					使用収益済面積	0.0	0.0	0.0	2.4	2.6	3.1	3.9	4.6	4.8	5.5	5.5	5.8		
				使用収益開始率				12.5%	13.8%	16.6%	20.5%	24.4%	25.4%	29.1%	29.3%	30.8%			
⑧	川口市	石神西立野	市	面積(ha)	99.1	99.1	99.1	99.1	99.1	99.1	99.1	99.1	99.1	99.1	99.1				
				施行期間	H6-H25	H6-H25	H6-H25	H6-H25	H6-H25	H6-H25	H6-H25	H6-H25	H6-H35	H6-H35	H6-H35	H6-H35			
				計画人口(人)	9,900	9,900	9,900	9,900	9,900	9,900	9,900	9,900	9,900	9,900	9,900	9,900			
				総事業費	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100		
					うち国庫補助等	19,510	19,510	19,510	19,510	19,510	19,510	19,510	19,510	20,384	20,384	20,384	20,384		
				事業費ベース	総事業費	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100	36,100		
					執行済額	0	6,895	4,513	5,054	5,704	5,848	6,751	8,014	9,169	10,216	10,974	11,769		
				進捗率			19.1%	12.5%	14.0%	15.8%	16.2%	18.7%	22.2%	25.4%	28.3%	30.4%	32.6%		
					仮換地指定率	仮換地総面積	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2		
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	57.0	57.3	58.1	58.8	58.9	59.3	59.4	59.9	59.8		
					仮換地指定率				90.2%	90.7%	92.0%	93.0%	93.2%	93.9%	94.0%	94.7%	94.6%		
				使用収益	仮換地総面積	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2	63.2		
					使用収益済面積	0.0	0.0	0.0	4.1	4.6	5.1	6.2	6.6	7.7	8.3	9.0	9.4		
				使用収益開始率				6.5%	7.2%	8.1%	9.8%	10.5%	12.2%	13.1%	14.2%	14.9%			

埼玉高速鉄道沿線土地区画整理事業進捗状況(施行中)

平成25年3月末現在

黄色着色部に入力をお願いします

号	市町村名	地区名	施行主体		13年度末	14年度末	15年度末	16年度末	17年度末	18年度末	19年度末	20年度末	21年度末	22年度末	23年度末	24年度末				
⑨	川口市	安行藤八	市	面積(ha)	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1	68.1			
				施行期間	H9-H23	H9-H23	H9-H26	H9-H26	H9-H26	H9-H26	H9-H26	H9-H26	H9-H26	H9-H26	H9-H26	H9-H36	H9-H36	H9-H36	H9-H36	
				計画人口(人)	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	6,800	
				総事業費	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675
					うち国庫補助等	19,147	19,147	19,147	19,147	19,147	19,147	19,147	19,147	19,147	19,147	19,147	20,403	20,403	20,403	20,403
				事業費ベース	総事業費	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675	30,675
					執行済額	0	3,896	920	1,166	1,319	1,564	2,025	2,638	3,190	3,712	4,110	4,632	4,632	4,632	4,632
				進捗率			12.7%	3.0%	3.8%	4.3%	5.1%	6.6%	8.6%	10.4%	12.1%	13.4%	15.1%	15.1%	15.1%	15.1%
					仮換地指定率	仮換地総面積	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9
				仮換地指定率	仮換地済面積	0.0	0.0	0.0	34.3	35.2	36.5	38.0	39.8	40.2	40.3	40.9	40.9	40.9	40.9	
					仮換地指定率				78.1%	80.2%	83.2%	86.6%	90.7%	91.5%	91.7%	93.1%	93.2%	93.2%	93.2%	
				使用収益	仮換地総面積	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9	43.9
					使用収益済面積	0.0	0.0	0.0	6.8	6.9	7.0	7.7	7.9	8.5	8.8	9.1	9.7	9.7	9.7	9.7
					使用収益開始率				15.6%	15.7%	16.0%	17.6%	18.1%	19.3%	20.1%	20.7%	22.0%	22.0%	22.0%	22.0%
				⑩	鳩ヶ谷市	里	市	面積(ha)	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7
施行期間	H1-H15	H1-H15	H1-H25					H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H25	H1-H35	
計画人口(人)	6,400	6,400	6,400					6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	
総事業費	37,590	37,590	27,280					37,590	37,600	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590
	うち国庫補助等	16,358	16,358					16,358	16,358	15,999	16,358	16,358	16,358	16,358	16,358	16,358	16,358	16,358	16,358	23,992
事業費ベース	総事業費	37,590	37,590					27,280	37,590	37,600	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590	37,590
	執行済額	0	16,991					13,640	16,502	18,311	19,697	21,163	21,840	23,419	24,885	25,975	26,802	26,802	26,802	26,802
進捗率			45.2%					50.0%	43.9%	48.7%	52.4%	56.3%	58.1%	62.3%	66.2%	69.1%	71.3%	71.3%	71.3%	71.3%
	仮換地指定率	仮換地総面積	51.7					51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7
仮換地指定率	仮換地済面積	0.0	0.0					0.0	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	
	仮換地指定率								100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	
使用収益	仮換地総面積	51.7	51.7					51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7
	使用収益済面積	0.0	0.0					0.0	9.2	11.8	12.1	13.4	14.9	19.4	21.4	23.5	24.1	24.1	24.1	
	使用収益開始率								17.8%	22.9%	23.4%	25.9%	28.8%	37.6%	41.4%	45.4%	46.6%	46.6%	46.6%	

埼玉高速鉄道沿線土地区画整理事業進捗状況(施行中)

平成25年3月末現在

黄色着色部に入力をお願いします

号	市町村名	地区名	施行主体	13年度末	14年度末	15年度末	16年度末	17年度末	18年度末	19年度末	20年度末	21年度末	22年度末	23年度末	24年度末	
合 計			面積(ha)	759.8	759.8	759.8	759.8	759.8	759.8	759.8	759.8	759.8	759.8	759.8	759.8	
			計画人口(人)	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070	71,070
			総事業費	287,476	287,476	287,991	295,021	295,159	290,181	290,181	290,181	292,910	292,910	292,910	293,720	
			うち国庫補助等	116,486	116,486	116,486	116,486	116,727	116,486	116,486	116,486	120,375	121,631	121,631	130,828	
			事業費ベース	総事業費	287,476	287,476	287,991	295,021	295,159	290,181	290,181	290,181	292,910	292,910	292,910	293,720
			執行済額	0	64,657	54,142	66,220	82,148	88,870	100,474	125,144	144,838	165,310	179,029	192,133	
			進捗率	0.0%	22.5%	18.8%	22.4%	27.8%	30.6%	34.6%	43.1%	49.4%	56.4%	61.1%	65.4%	
			仮換地指定率	仮換地総面積	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9
			仮換地済面積	0.0	0.0	0.0	322.5	343.6	356.3	362.4	363.7	370.9	384.5	405.5	429.6	
			仮換地指定率	0.0%	0.0%	0.0%	71.4%	76.0%	78.9%	80.2%	80.5%	82.1%	85.1%	89.7%	95.1%	
			使用収益	面積	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	451.9	
			使用収益済面積	0.0	0.0	0.0	46.4	65.6	78.6	84.9	92.6	104.8	110.8	117.5	138.3	
			使用収益開始率	0.0%	0.0%	0.0%	10.3%	14.5%	17.4%	18.8%	20.5%	23.2%	24.5%	26.0%	30.6%	
さいたま市計			面積(ha)	425.5	425.5	425.5	425.5	425.5	425.5	425.5	425.5	425.5	425.5	425.5	425.5	
			計画人口(人)	41,700	41,700	41,700	41,700	41,700	41,700	41,700	41,700	41,700	41,700	41,700	41,700	
			総事業費	152,396	152,396	163,221	159,941	160,320	155,352	155,352	155,352	157,759	157,759	157,759	157,759	
			うち国庫補助等	46,988	46,988	46,988	46,988	47,988	46,988	46,988	46,988	49,142	49,142	49,142	49,142	
			事業費ベース	総事業費	152,396	152,396	163,221	159,941	160,320	155,352	155,352	155,352	157,759	157,759	157,759	
			執行済額	0	21,148	22,043	27,758	40,199	42,132	49,733	70,230	85,451	102,000	112,974	123,175	
			進捗率	0.0%	13.9%	13.5%	17.4%	25.1%	27.1%	32.0%	45.2%	54.2%	64.7%	71.6%	78.1%	
			仮換地指定率	仮換地総面積	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	
			仮換地済面積	0.0	0.0	0.0	125.6	145.4	156.0	159.9	159.3	165.7	179.2	199.1	223.2	
			仮換地指定率	0.0%	0.0%	0.0%	52.5%	60.8%	65.2%	66.9%	66.6%	69.3%	74.9%	83.3%	93.3%	
			使用収益	面積	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	239.1	
			使用収益済面積	0.0	0.0	0.0	0.0	14.5	23.2	24.5	29.4	33.3	34.9	38.5	57.4	
			使用収益開始率	0.0%	0.0%	0.0%	0.0%	6.1%	9.7%	10.3%	12.3%	13.9%	14.6%	16.1%	24.0%	
川口市計			面積(ha)	253.6	253.6	253.6	253.6	253.6	253.6	253.6	253.6	253.6	253.6	253.6	253.6	
			計画人口(人)	22,970	22,970	22,970	22,970	22,970	22,970	22,970	22,970	22,970	22,970	22,970	22,970	
			総事業費	97,490	97,490	97,490	97,490	97,239	97,239	97,239	97,239	97,561	97,561	97,561	98,371	
			うち国庫補助等	53,140	53,140	53,140	53,140	53,140	53,140	53,140	53,140	54,875	56,131	56,131	57,694	
			事業費ベース	総事業費	97,490	97,490	97,490	97,490	97,239	97,239	97,239	97,239	97,561	97,561	97,561	
			執行済額	0	26,518	18,459	21,960	23,639	27,041	29,578	33,075	35,969	38,425	40,080	42,155	
			進捗率	0.0%	27.2%	18.9%	22.5%	24.3%	27.8%	30.4%	34.0%	36.9%	39.4%	41.1%	42.9%	
			仮換地指定率	仮換地総面積	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	
			仮換地済面積	0.0	0.0	0.0	145.2	146.5	148.7	150.8	152.7	153.5	153.7	154.7	154.7	
			仮換地指定率	0.0%	0.0%	0.0%	90.1%	90.9%	92.3%	93.6%	94.8%	95.3%	95.4%	96.0%	96.0%	
			使用収益	面積	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	161.1	
			使用収益済面積	0.0	0.0	0.0	37.2	39.2	43.3	47.0	48.3	52.1	54.4	55.5	56.9	
			使用収益開始率	0.0%	0.0%	0.0%	23.1%	24.3%	26.9%	29.1%	30.0%	32.3%	33.8%	34.4%	35.3%	
鳩ヶ谷市			面積(ha)	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	80.7	
			計画人口(人)	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	6,400	
			総事業費	37,590	37,590	27,280	37,590	37,600	37,590	37,590	37,590	37,590	37,590	37,590	37,590	
			うち国庫補助等	16,358	16,358	16,358	16,358	15,599	16,358	16,358	16,358	16,358	16,358	16,358	23,992	
			事業費ベース	総事業費	37,590	37,590	27,280	37,590	37,600	37,590	37,590	37,590	37,590	37,590	37,590	
			執行済額	0	16,991	13,640	16,502	18,311	19,697	21,163	21,840	23,419	24,885	25,975	26,802	
			進捗率	0.0%	45.2%	50.0%	43.9%	48.7%	52.4%	56.3%	58.1%	62.3%	66.2%	69.1%	71.3%	
			仮換地指定率	仮換地総面積	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	
			仮換地済面積	0.0	0.0	0.0	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	
			仮換地指定率	0.0%	0.0%	0.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	
			使用収益	面積	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	51.7	
			使用収益済面積	0.0	0.0	0.0	9.2	11.8	12.1	13.4	14.9	19.4	21.4	23.5	24.1	
			使用収益開始率	0.0%	0.0%	0.0%	17.8%	22.9%	23.4%	25.9%	28.8%	37.6%	41.4%	45.4%	46.6%	

※1 データは、平成25年度「彩の国の区画整理」(H25.6作成予定)から。

※2 国庫補助等は、基本事業費、一般会計補助事業費、地方特定道路整備事業の合計。
